

ABC Company
Project V-999

ID	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Jan 28, '07						
							W	T	F	S	S	M	T
1	ABC Company Order Received	107 days	Fri 1/26/07	Mon 6/25/07		ABC Company							
2	ABC Order Processed	4 days	Fri 1/26/07	Wed 1/31/07		White Systems							
3	Engineering	21 days	Thu 2/1/07	Thu 3/1/07									
4	Mechanical	21 days	Thu 2/1/07	Thu 3/1/07	2	White Systems							
5	Electrical	8 days	Mon 2/19/07	Wed 2/28/07	2	White Systems							
6	Order 3 Party Components	21 days	Mon 3/5/07	Mon 4/2/07									
7	Conveyor Components	1 day	Mon 3/5/07	Mon 3/5/07	2	Bastian							
8	Rolling Ladders	1 day	Mon 3/5/07	Mon 3/5/07	2	Grainger							
9	Bin Totes	1 day	Mon 3/5/07	Mon 3/5/07	2	Flexcon							
10	Computer Hardware	1 day	Mon 4/2/07	Mon 4/2/07	2	Dell							
11	Manufacturing	39 days	Thu 3/1/07	Tue 4/24/07									
12	Mechanical Components	38 days	Fri 3/2/07	Tue 4/24/07									
13	Track Section	38 days	Fri 3/2/07	Tue 4/24/07	4	White Systems							
14	Bin Components	30 days	Fri 3/2/07	Thu 4/12/07	4	White Systems							
15	Electrical Components	38 days	Thu 3/1/07	Mon 4/23/07									
16	Control Panels	38 days	Thu 3/1/07	Mon 4/23/07	5	White Systems							
17	Motor Drive Assemblies	10 days	Mon 4/2/07	Fri 4/13/07	5	White Systems							
18	Shipping	8 days	Wed 4/25/07	Fri 5/4/07									
19	Carousels	1 day	Fri 4/27/07	Fri 4/27/07	11	White Systems							
20	Conveyor	1 day	Fri 5/4/07	Fri 5/4/07	7	Bastian							
21	Rolling Ladders	1 day	Wed 4/25/07	Wed 4/25/07	6	Grainger							
22	Bin Totes	1 day	Tue 5/1/07	Tue 5/1/07	9	Flexcon							
23	Receive Material	8 days	Wed 5/2/07	Fri 5/11/07									
24	Carousels	1 day	Wed 5/2/07	Wed 5/2/07	19	ABC Company							
25	Conveyor	1 day	Fri 5/11/07	Fri 5/11/07	20	ABC Company							
26	Rolling Ladders	1 day	Fri 5/4/07	Fri 5/4/07	21	ABC Company							
27	Bin Totes	1 day	Mon 5/7/07	Mon 5/7/07	22	ABC Company							
28	Installation	11 days	Tue 5/15/07	Tue 5/29/07									
29	Install Track Sections	6 days	Tue 5/15/07	Tue 5/22/07	23	White Systems							

Project:2007 Web Site.mpp
Date: Tue 7/24/07

Task

Milestone

External Tasks

Split

Summary

External Milestone










Progress

Project Summary


Deadline

ABC Company
Project V-999

ID	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Jan 28, '07											
							W	T	F	S	S	M	T	W	T	F		
30	Assemble Bins	5 days	Wed 5/16/07	Tue 5/22/07	23	White Systems												
31	Install Bins	3 days	Wed 5/23/07	Fri 5/25/07	30	White Systems												
32	Install Control Panels	1 day	Thu 5/17/07	Thu 5/17/07	23	White Systems												
33	Wire Carousels	6 days	Thu 5/17/07	Thu 5/24/07		White Systems												
34	Commission Carousels	1 day	Fri 5/25/07	Fri 5/25/07	33	White Systems												
35	Install Conveyor	1 day	Tue 5/22/07	Tue 5/22/07	23	White Systems												
36	Install Rolling Ladders	1 day	Wed 5/23/07	Wed 5/23/07	29	White Systems												
37	Carousels Ready for SW	1 day	Tue 5/29/07	Tue 5/29/07	34	White Systems												
38	Software	79 days	Tue 3/6/07	Fri 6/22/07														
39	Kick Off Meeting	1 day	Tue 3/6/07	Tue 3/6/07	2	ABC Comp / White Sy												
40	PC HW Shipped to NJ	1 day	Wed 4/18/07	Wed 4/18/07	10	Dell												
41	Load SW on PC's	5 days	Tue 5/1/07	Mon 5/7/07	40	White Systems												
42	Test PC in Lab	3 days	Tue 5/8/07	Thu 5/10/07	41	White Systems												
43	Ship PC to ABC Company	1 day	Fri 5/11/07	Fri 5/11/07	42	White Systems												
44	Pilot Install / SW Training	3 days	Wed 5/30/07	Fri 6/1/07	37,42	ABC Comp / White Sy												
45	SW Testing	15 days	Mon 6/4/07	Fri 6/22/07	44	ABC Comp / White Sy												
46	SW Go Live	1 day	Mon 6/25/07	Mon 6/25/07	45	ABC Company												

Project:2007 Web Site.mpp Date: Tue 7/24/07	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	


ABC Company
Project V-999

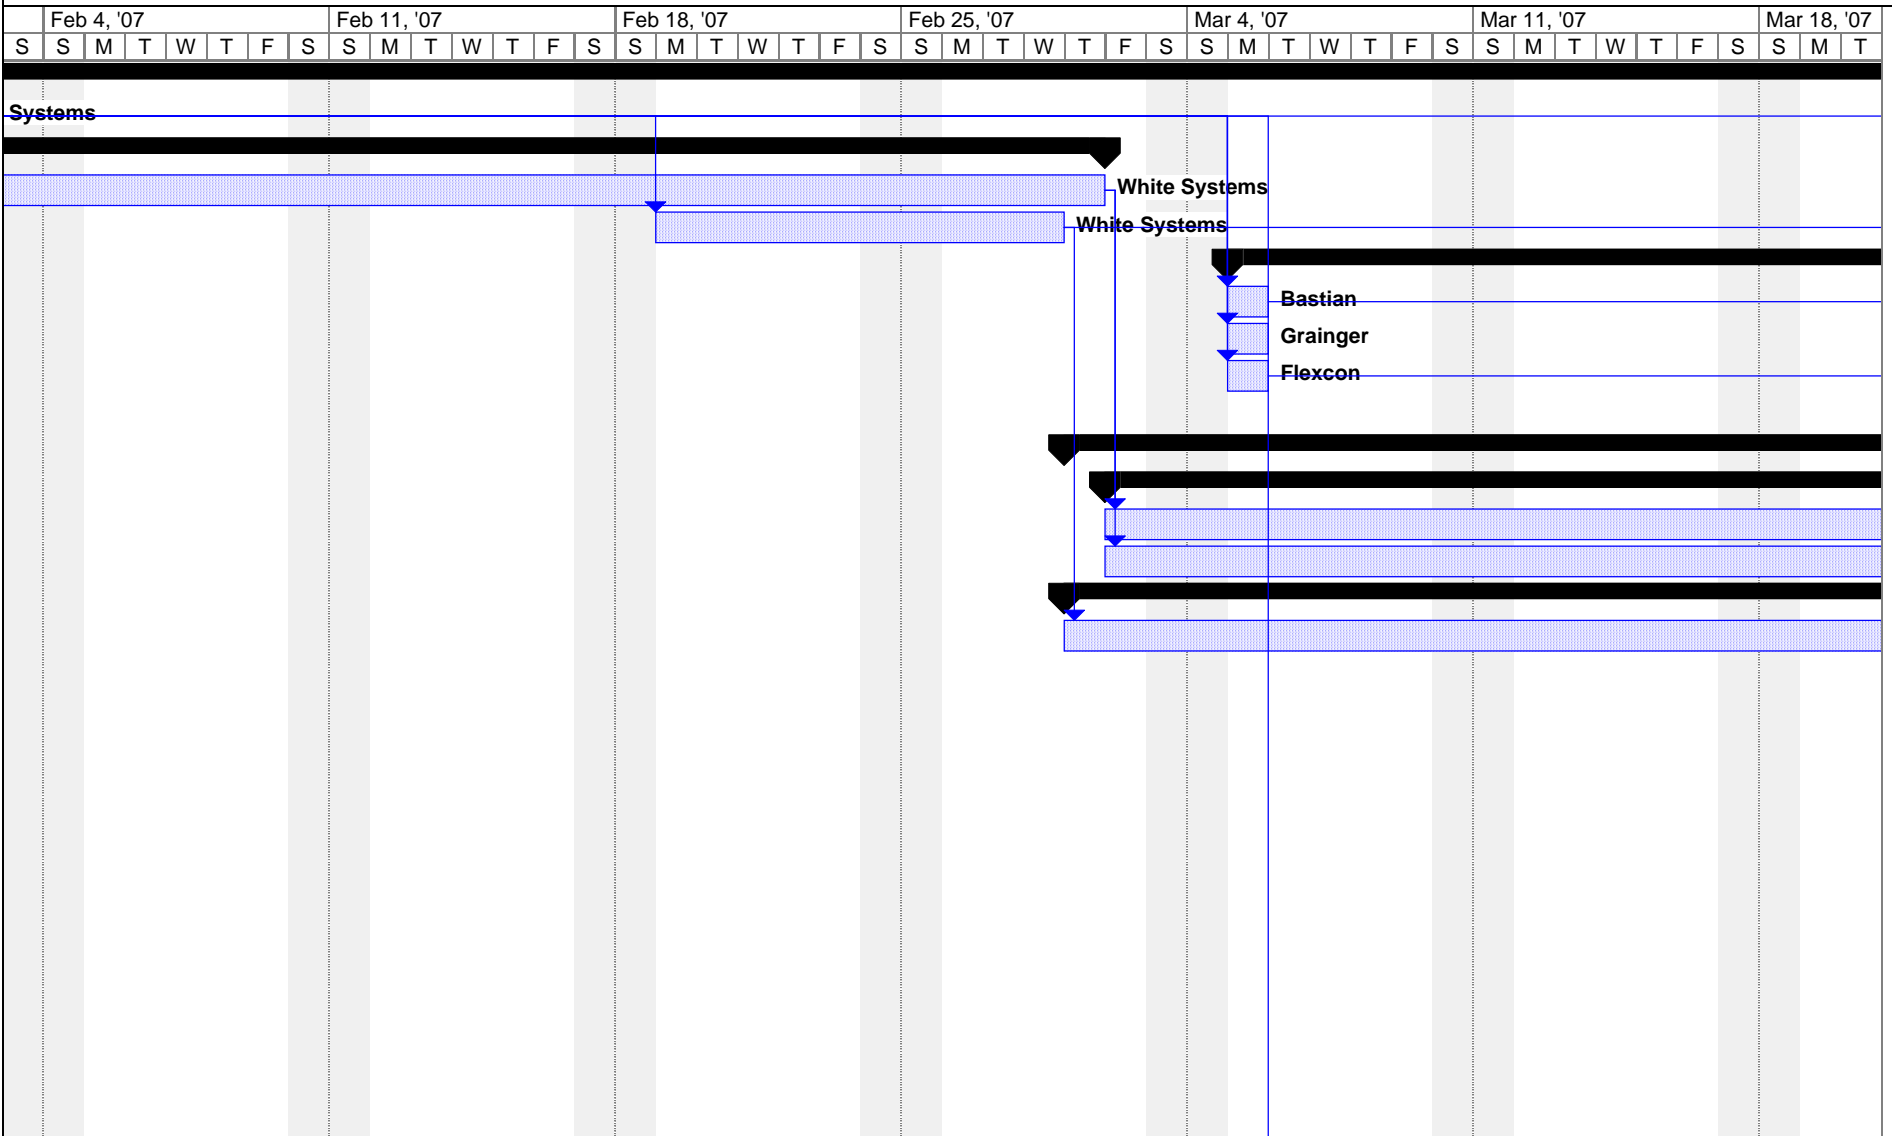

Project:2007 Web Site.mpp
Date: Tue 7/24/07


Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

ABC Company
Project V-999

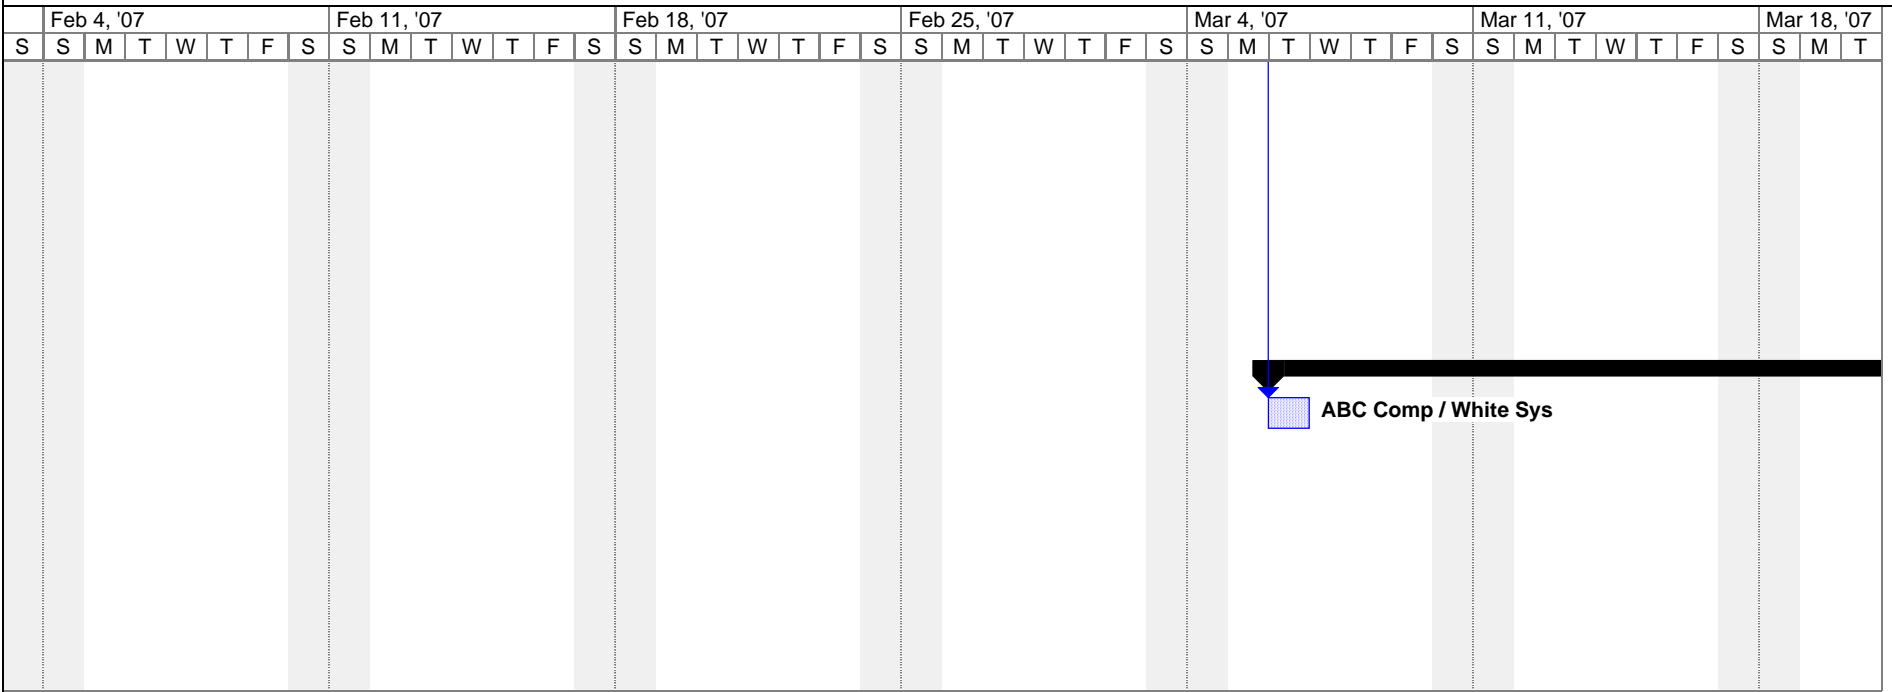


Project:2007 Web Site.mpp Date: Tue 7/24/07	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

ABC Company
Project V-999

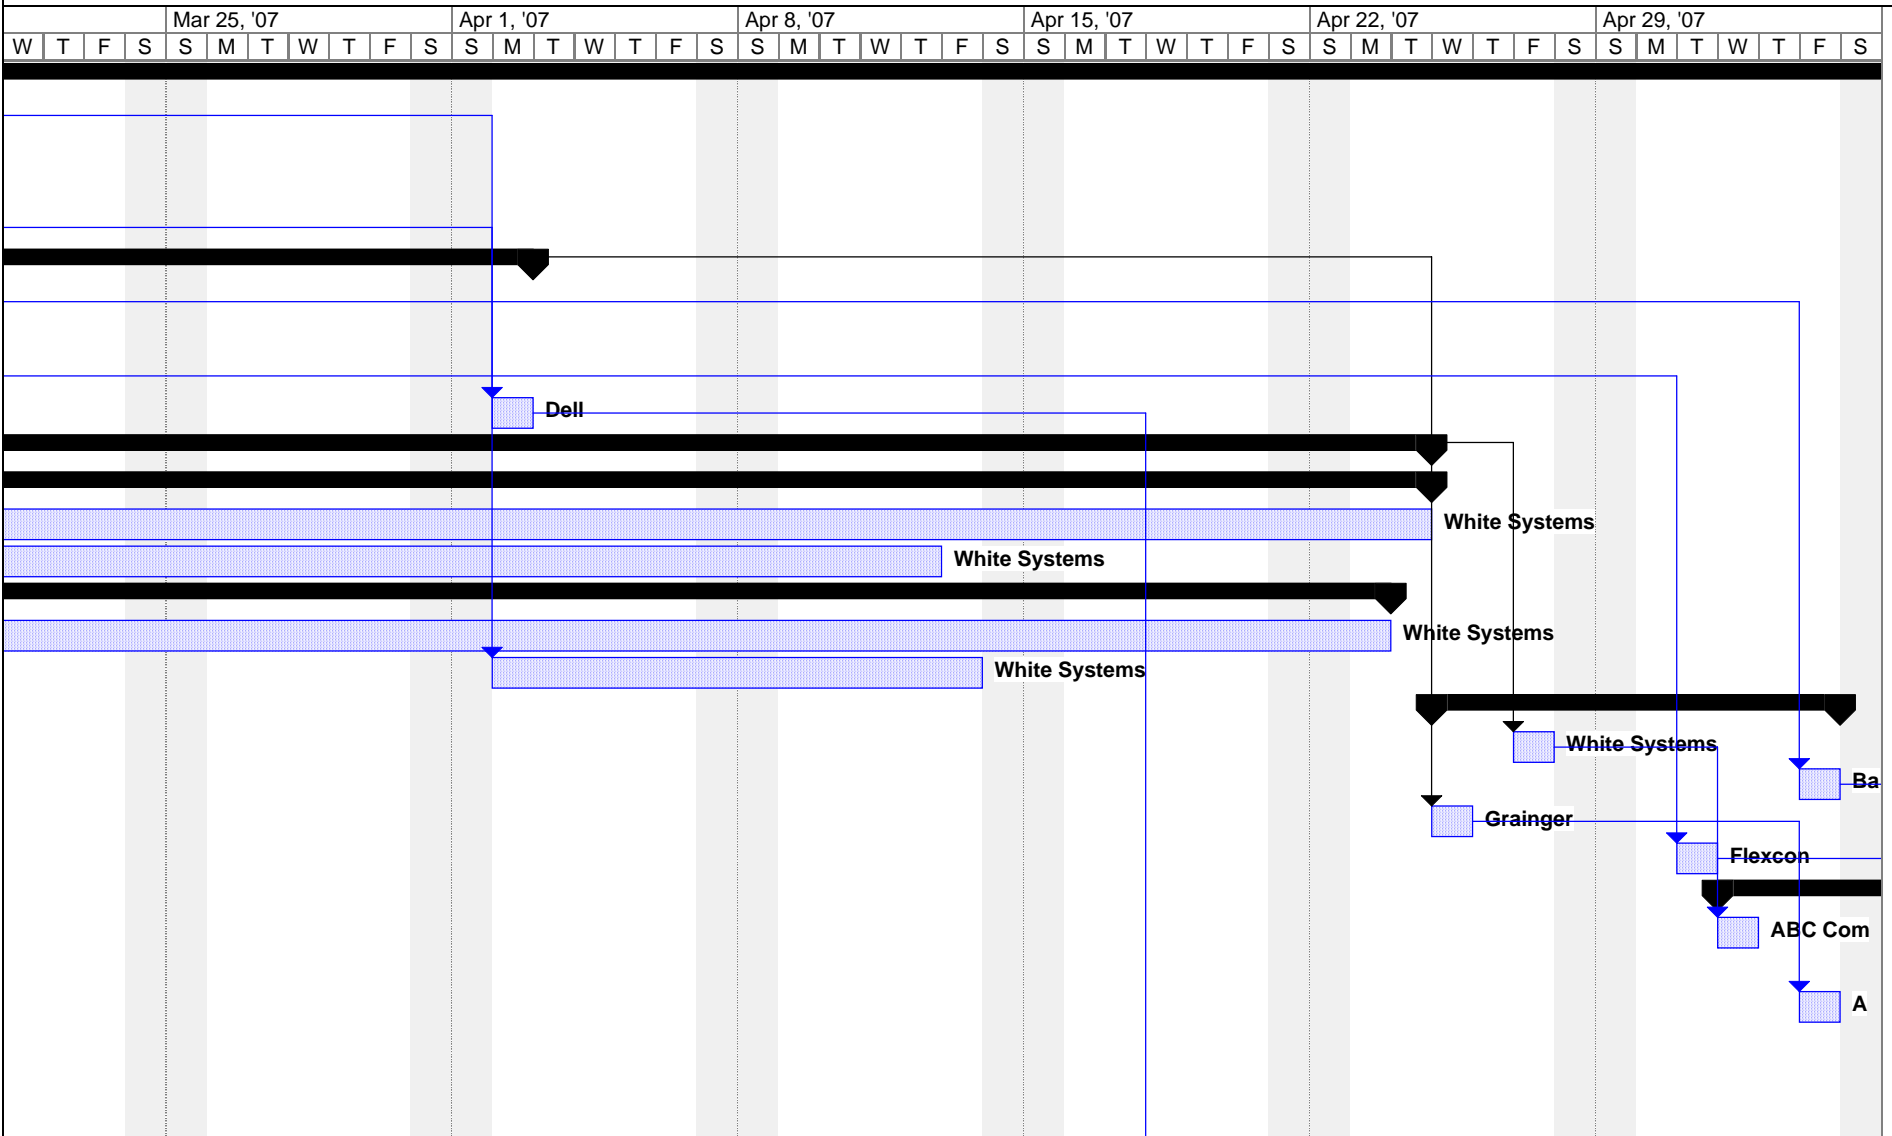





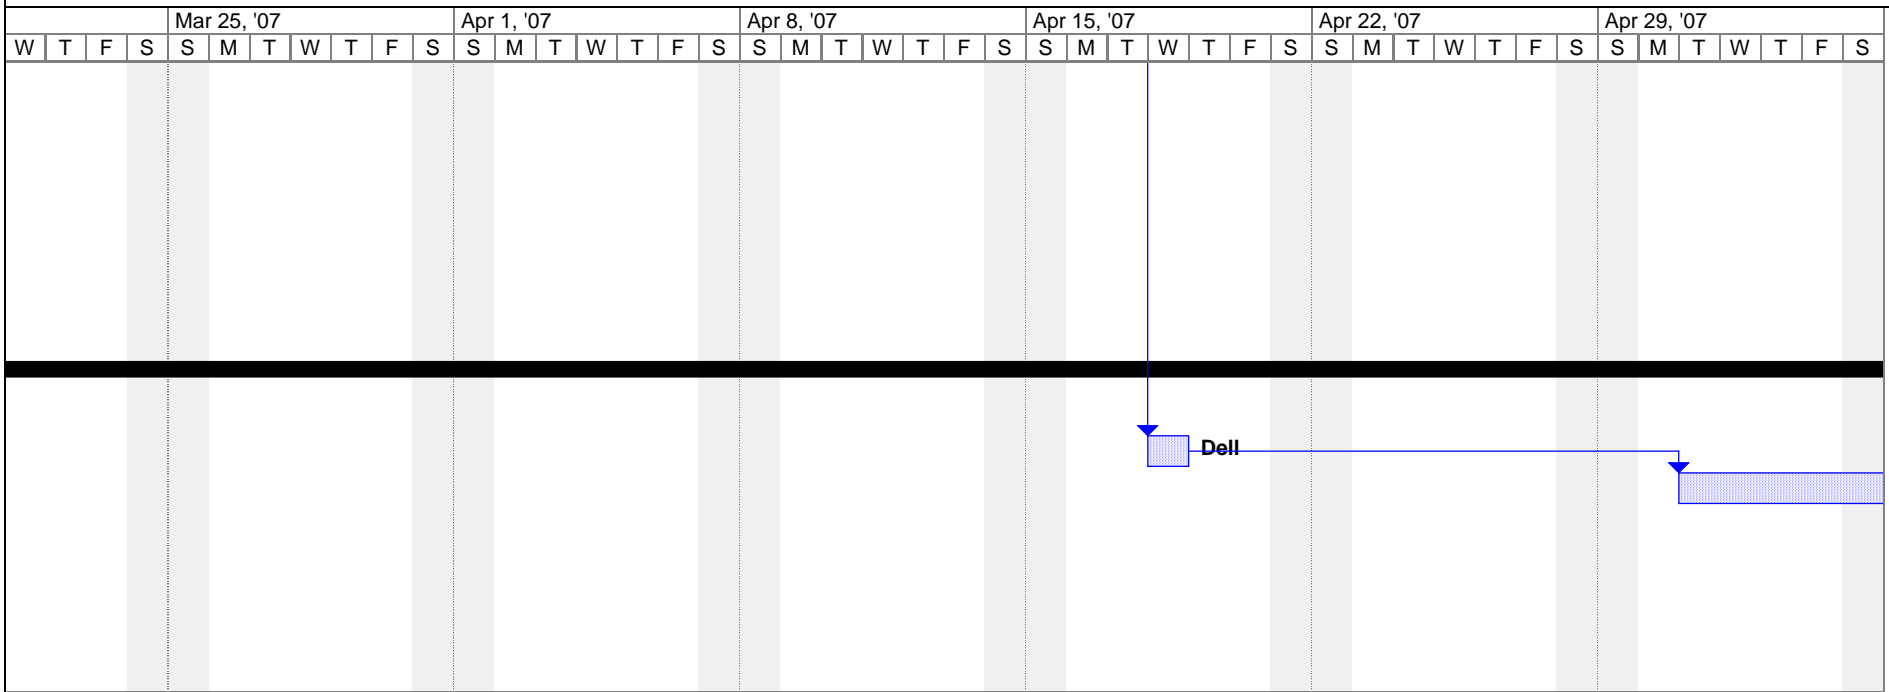




Project:2007 Web Site.mpp
Date: Tue 7/24/07

ABC Company
Project V-999




Project:2007 Web Site.mpp
Date: Tue 7/24/07

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	


ABC Company
Project V-999

May 6, '07							May 13, '07							May 20, '07							May 27, '07							Jun 3, '07							Jun 10, '07							Jun 17, '07				
S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	

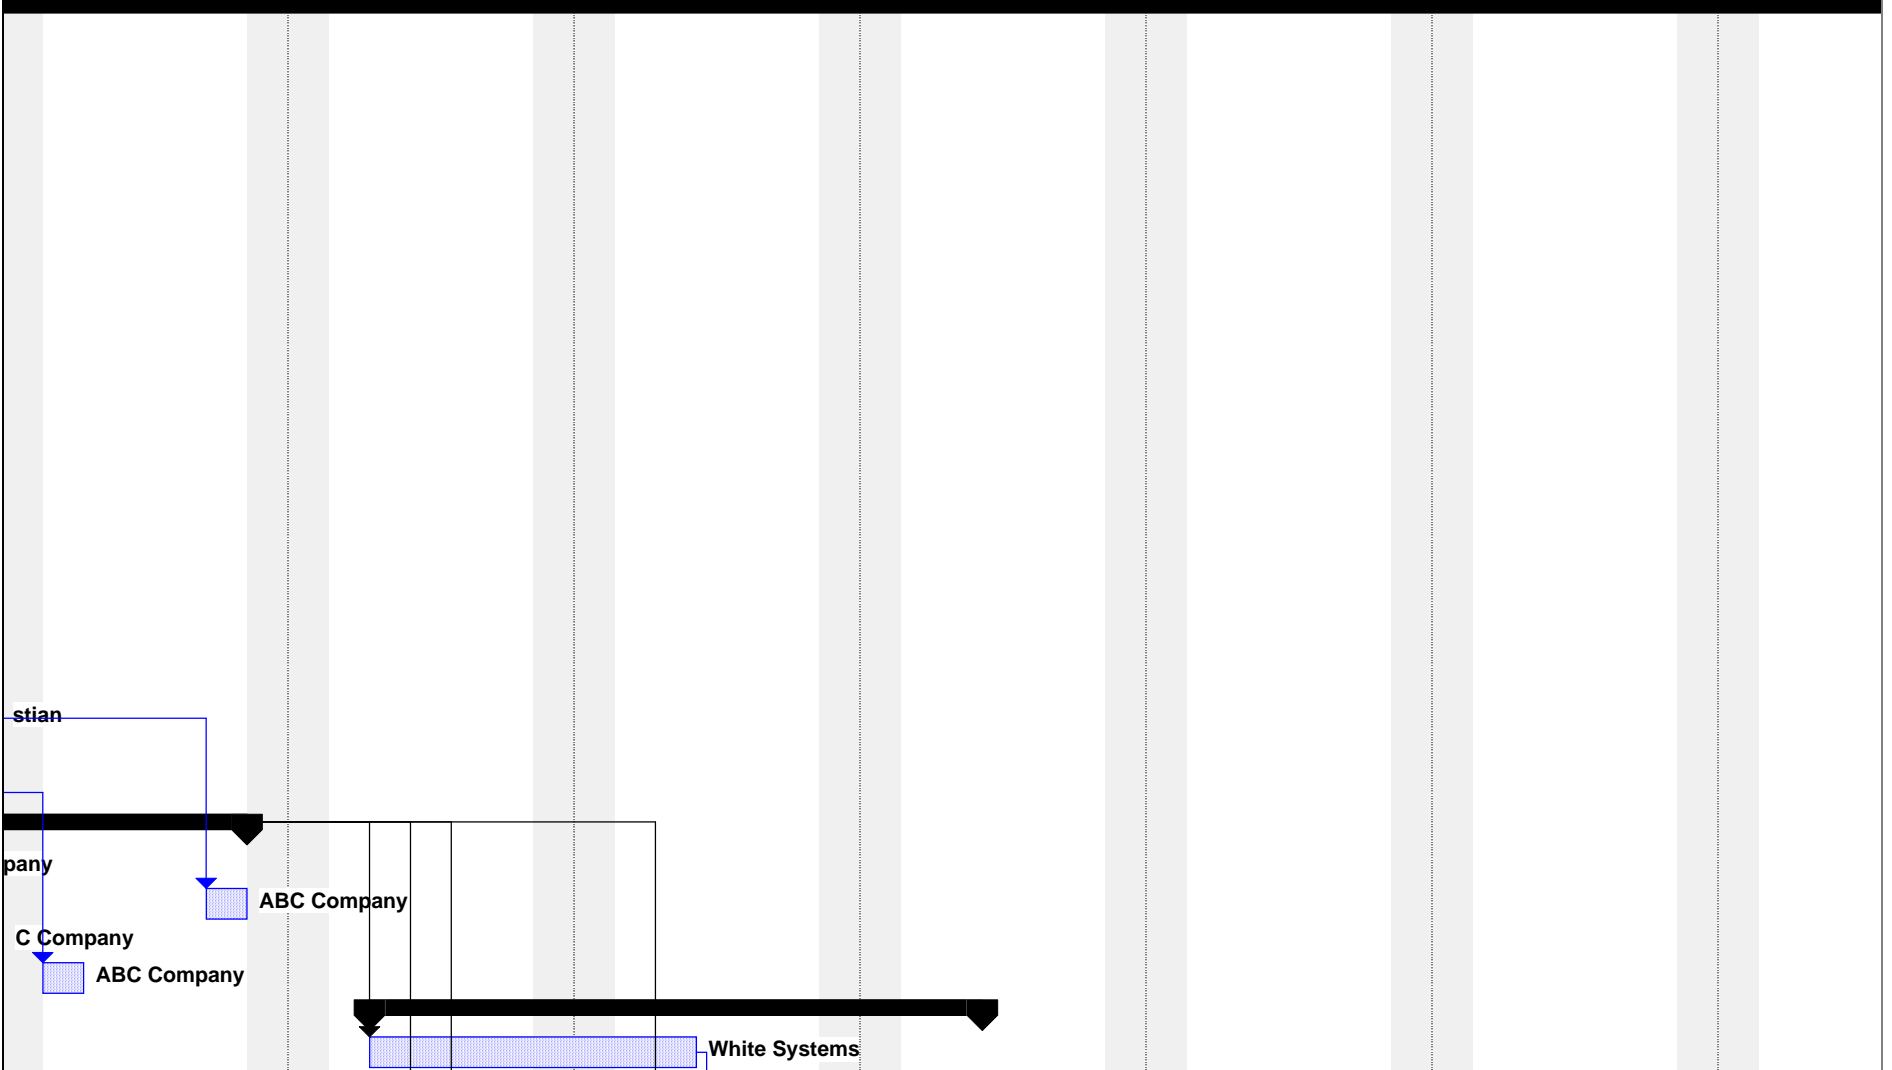





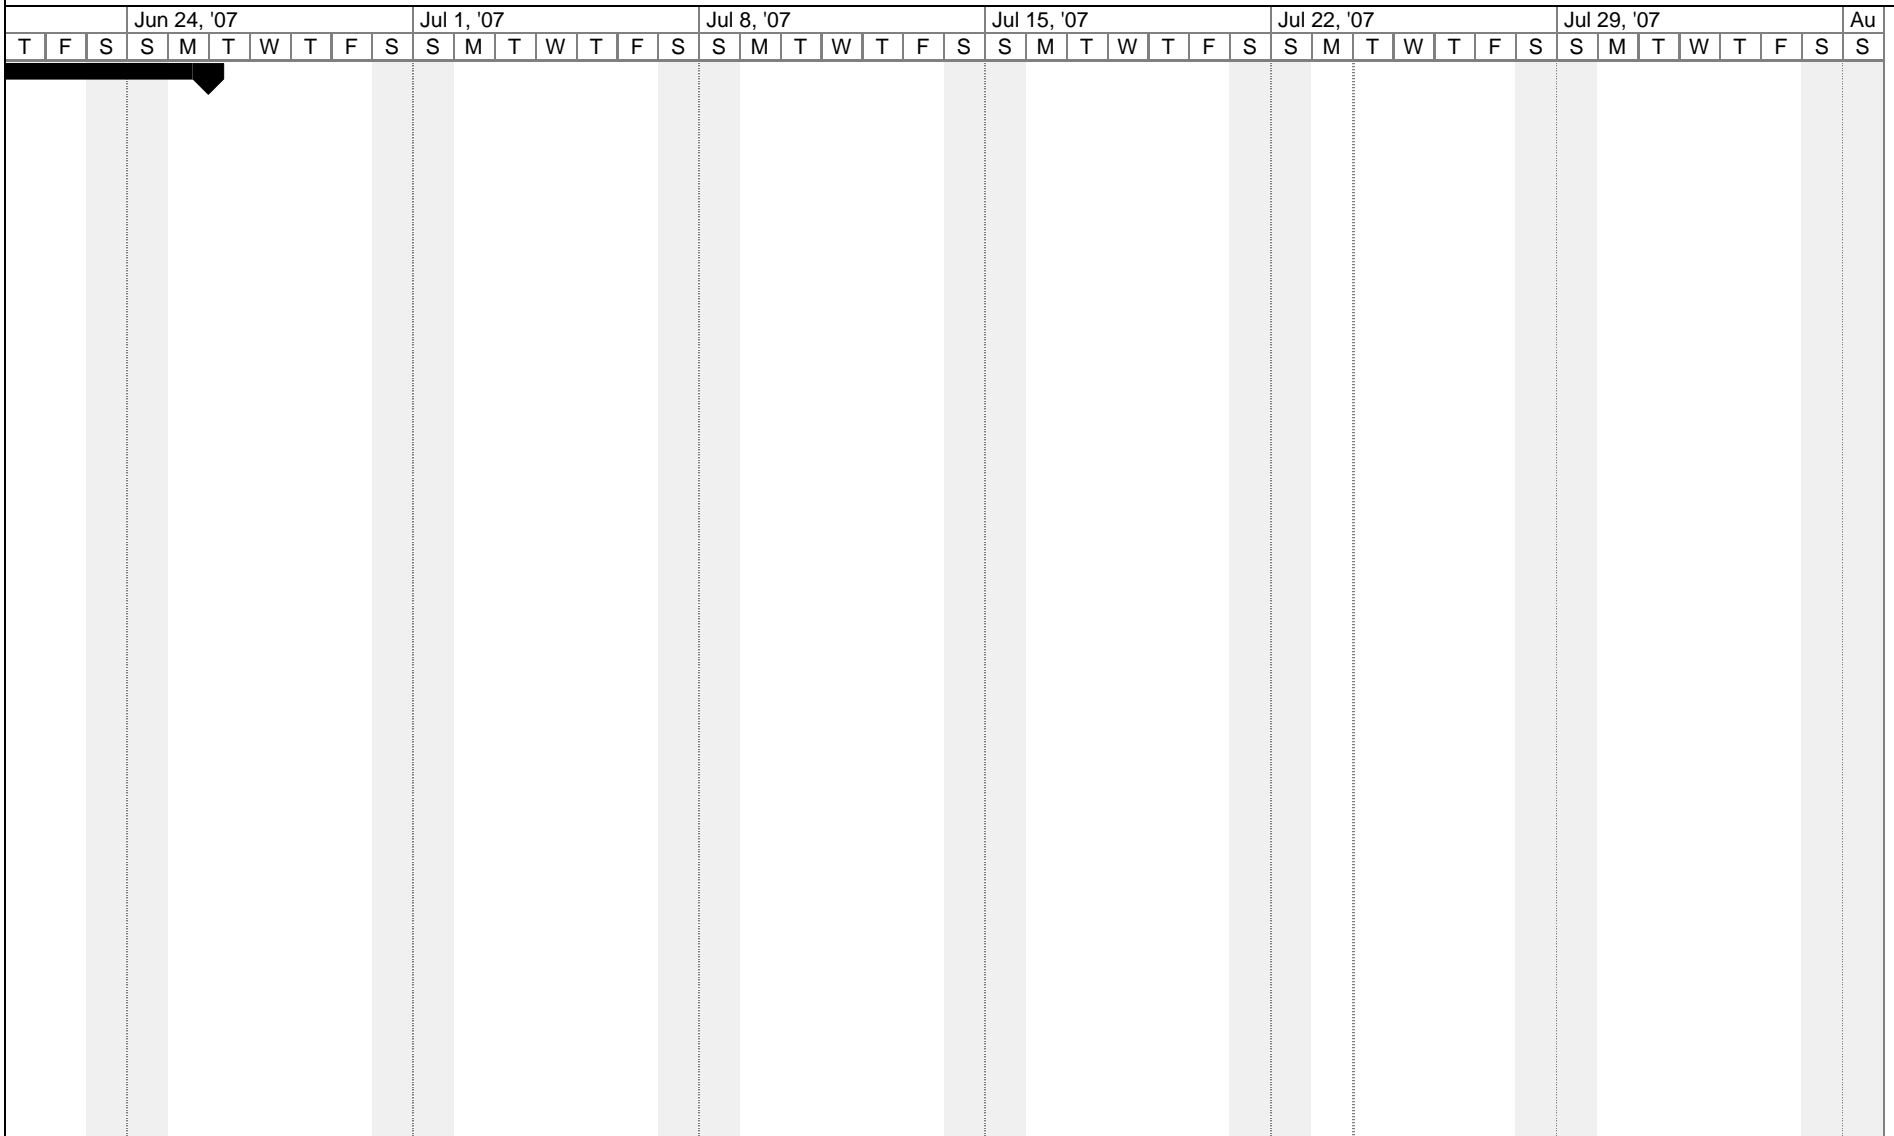



Project:2007 Web Site.mpp Date: Tue 7/24/07	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

ABC Company
Project V-999



Project:2007 Web Site.mpp
Date: Tue 7/24/07

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	
